

Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473

Brooks, Alberta

T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862



INSPECTION REPORT

Client: Four Star Ventures	Location: DaPaJo Construction Limited	Date: April 05, 2012
P.O. :	Work Order : 21391	Report : 3482
Page : 1 of 1	Rig or Unit :#12	Inspection: Magnetic Particle
Parts Examined: 7" Web Wilson 50 Ton elevator	S/N: 07420041	
Surface Condition: Painted	Material Temperature: 20° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaflix 7HF prepared bath		


Test Results:

Engineer's Approval:

Crack found on safety ear (crack repaired and elevator is ready for service)



Photos:

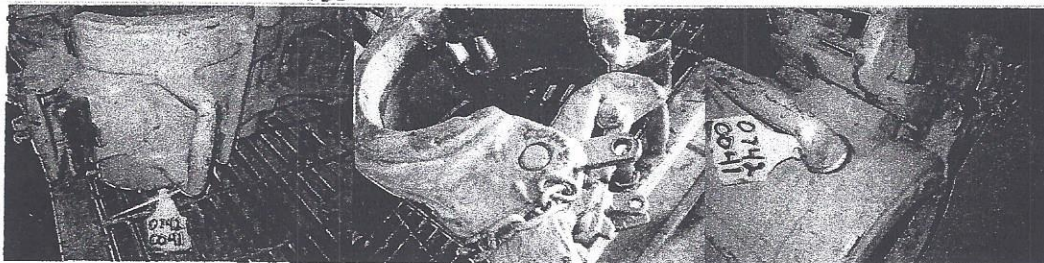

Technician: John Frances	CGSB #: 7062	Signature:	Assistant: Tyler Nevison
Repairs Complete	Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>	N/A	Acceptable For Service Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>
