

412

# Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)  
P.O Box 1473  
Brooks, Alberta  
T1R 1C3  
Phone: 403-362-2843 Fax: 403-362-2862

# INSPECTION REPORT

Client: 4 Star Ventures	Location: DaPaJo Construction Limited	Date: October 21, 2014
Page: 1 of 1	Unit :80822	Inspection: Magnetic Particle
Work Order:2520F	Report:4272	
Parts Examined: 4 1/2" AOT Casing Elevator		
Surface Condition: Painted	Material Temperature: 18° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaglo 14AM prepared bath		


**Test Results:**

No cracks found at time of inspection

**Engineer's Approval:**



**Photos:**

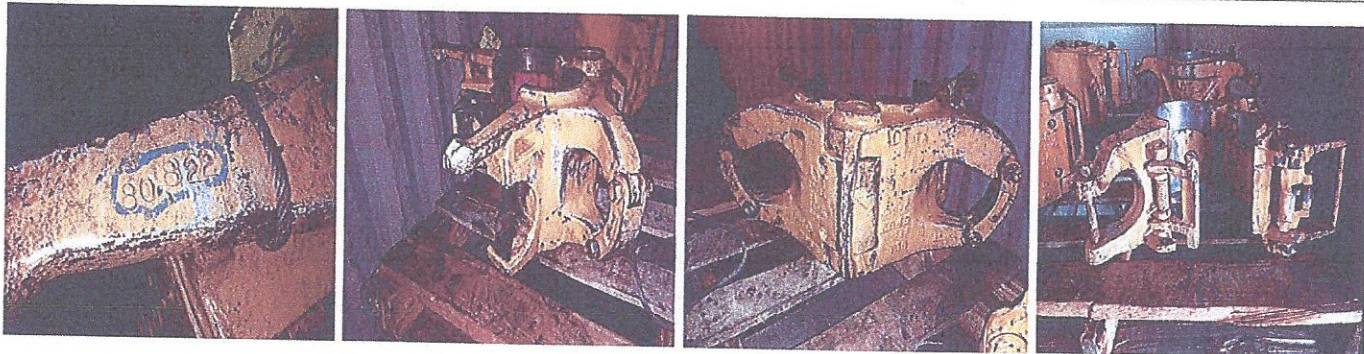

Technician: Bryan Hoskins	CGSB #: 19053	Signature: <i>Bryan Hoskins</i>	Assistant: Travis Bungay
Repairs Complete	Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input checked="" type="checkbox"/> X	Acceptable For Service	
		Yes <input type="checkbox"/>	X <input checked="" type="checkbox"/> No <input type="checkbox"/>
