

Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473


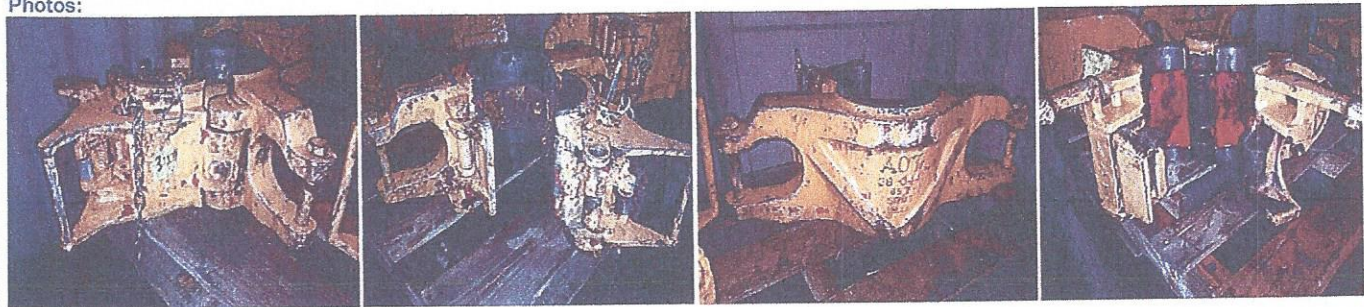

Brooks, Alberta

T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

INSPECTION REPORT

Client: 4 Star Ventures	Location: DaPaJo Construction Limited	Date: October 21, 2014
Page: 1 of 1	Unit :30271	Inspection: Magnetic Particle
Work Order:2520A	Report:4267	
Parts Examined: 5 1/2 AOT Casing Elevator		
Surface Condition: Painted	Material Temperature: 18° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaglo 14AM prepared bath		
Test Results:	Engineer's Approval:	
No cracks found at time of inspection		
Photos:		
		
Technician: Bryan Hoskins	CGSB #: 19053	Signature: 
		Assistant: Travis Bungay
Repairs Complete	Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input type="checkbox"/> X <input checked="" type="checkbox"/>	Acceptable For Service Yes <input type="checkbox"/> X <input checked="" type="checkbox"/> No <input type="checkbox"/>
