


Ideal Inspection
 (a division of Ideal Oilfield Construction Ltd.)
 P.O Box 1473
 Brooks, Alberta
 T1R 1C3
 Phone: 403-362-2843 Fax: 403-362-2862

INSPECTION REPORT

Client: Four Star Ventures Location: DaPaJo Construction Limited Date: April 05, 2012
 P.O.: Work Order: 2139e Report: 3475
 Page: 1 of 1 Rig or Unit :#1 Inspection: Magnetic Particle
 Parts Examined: 2 7/8" BJ 65 Ton elevator S/N: EDM109830262021LT
 Surface Condition: Painted Material Temperature: 20° Celsius
 Procedure: MPI-DPJ-001 Code: ASME Section V, ASTM E709
 Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets
 Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method
 Test Medium: Magnaflux 7HF prepared bath

Test Results: Engineer's Approval:
 No defects found at time of inspection.

Professional Engineer M. FIRTH CALGARY SASKATCHEWAN
 PROFESSIONAL ENGINEER OF PROVINCE OF BRITISH COLUMBIA MARK FIRTH
 PROFESSIONAL ENGINEER ALBERTA MARK FIRTH
 PERMIT TO PRACTICE FIRTH ENGINEERING LTD
 Signature: [Signature] Date: [Signature]
 PERMIT NUMBER: P 6554
 The Association of Professional Engineers, Geologists and Geophysicists of Alberta

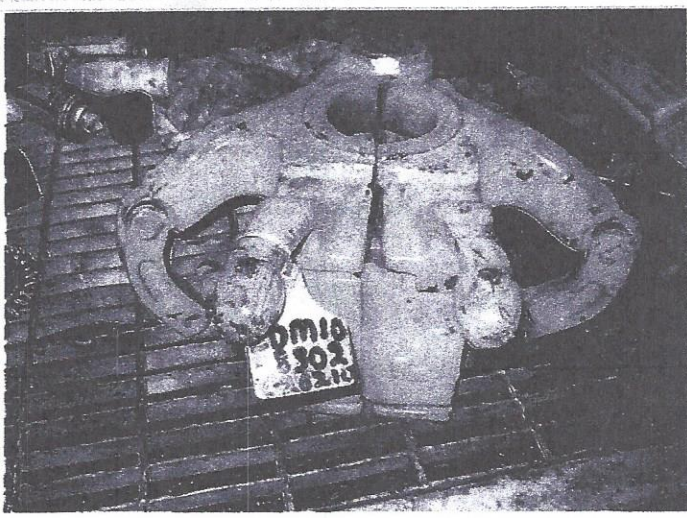

Photos:

Technician:	John Frances	CGSB #:	7062	Signature:		Assistant:	Tyler Nevison	
Repairs Complete	Yes	No	N/A	X	Acceptable For Service	Yes	X	No
