



Ideal Inspection
 (a division of Ideal Oilfield Construction Ltd.)
 P.O Box 1473
 Brooks, Alberta
 T1R 1C3
 Phone: 403-362-2843 Fax: 403-362-2862

INSPECTION REPORT

| | | |
|--|---------------------------------------|-------------------------------|
| Client: Four Star Ventures | Location: DaPaJo Construction Limited | Date: April 05, 2012 |
| P.O.: | Work Order : 2139q | Report : 3487 |
| Page : 1 of 1 | Rig or Unit : #5A | Inspection: Magnetic Particle |
| Parts Examined: 4 1/2" elevator | S/N: JKL-05-21-12 | |
| Surface Condition: Painted | Material Temperature: 20° Celsius | |
| Procedure: MPI-DPJ-001 | Code: ASME Section V, ASTM E709 | |
| Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets | | |
| Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method | | |
| Test Medium: Magnaflux 7HF prepared bath | | |

Test Results:
 No defects found at time of inspection.

Engineer's Approval:




PERMIT TO PRACTICE
FIRTH ENGINEERING LTD.

Signature: *[Signature]*

Date: *[Signature]*

PERMIT NUMBER: P 6554
 The Association of Professional Engineers,
 Geologists and Geophysicists of Alberta

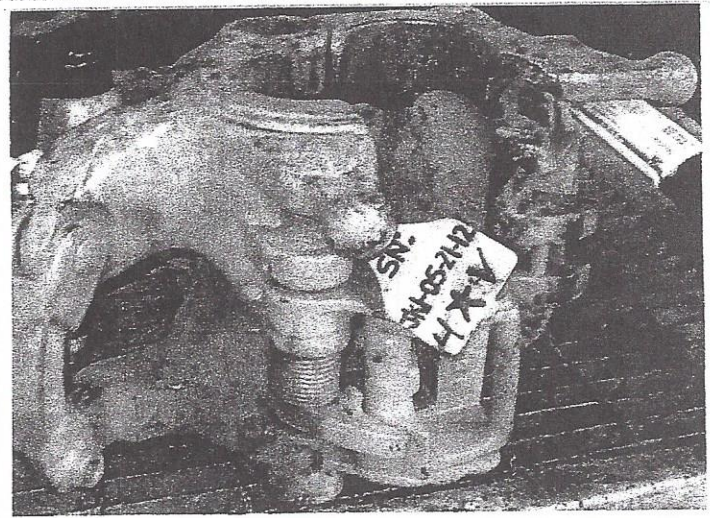

Photos:

| | | | |
|--------------------------|---|------------------------|--|
| Technician: John Frances | CGSB #: 7062 | Signature: | Assistant: Tyler Nevison |
| Repairs Complete | Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input type="checkbox"/> X <input checked="" type="checkbox"/> | Acceptable For Service | Yes <input type="checkbox"/> X <input checked="" type="checkbox"/> No <input type="checkbox"/> |
