

**Ideal Inspection**  
 (a division of Ideal Oilfield Construction Ltd.)  
 P.O Box 1473  
 Brooks, Alberta  
 T1R 1C3  
 Phone: 403-362-2843 Fax: 403-362-2862

702


# INSPECTION REPORT

Client: Four Star Ventures Location: DaPaJo Construction Limited Date: April 06, 2012  
 P.O. : Work Order : 2139b Report: 3472  
 Page: 1 of 1 Rig or Unit :#2 *A* Inspection: Magnetic Particle  
 Parts Examined: 7" AOT 65 Ton elevator S/N: 32751  
 Surface Condition: Painted Material Temperature: 20° Celsius  
 Procedure: MPI-DPJ-001 Code: ASME Section V, ASTM E709  
 Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets  
 Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method  
 Test Medium: Magnaflux 7HF prepared bath


**Test Results:**

No defects found at time of inspection

**Engineer's Approval:**



**PERMIT TO PRACTICE**  
**FIRTH ENGINEERING LTD**  
 Signature: *[Signature]*  
 Date: *April 12*  
**PERMIT NUMBER: P 6554**  
 The Association of Professional Engineers,  
 Geologists and Geophysicists of Alberta

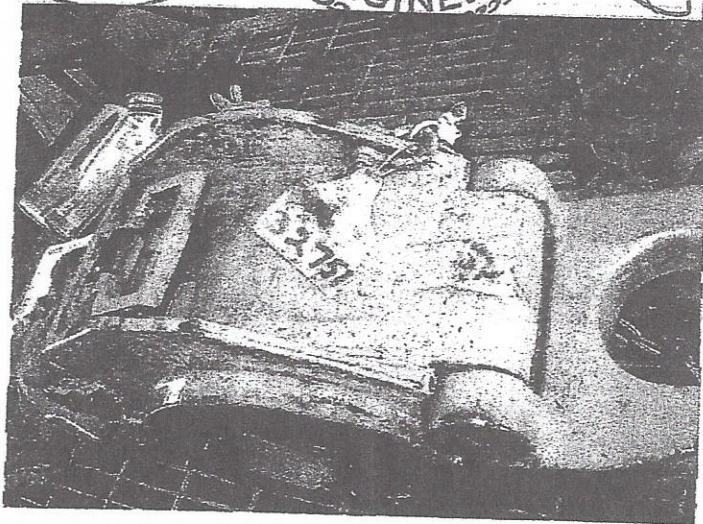

Photos:

Technician:	John Frances	CGSB #:	7062	Signature:		Assistant:	Tyler Nevison		
Repairs Complete	Yes	No	N/A	X		Acceptable For Service	Yes	X	No
