

Ideal Inspection
 (a division of Ideal Oilfield Construction Ltd.)
 P.O Box 1473
 Brooks, Alberta
 T1R 1C3
 Phone: 403-362-2843 Fax: 403-362-2862



INSPECTION REPORT

Client: Four Star Ventures Location: DaPaJo Construction Limited Date: April 05, 2012
 P.O. : Work Order : 2139a Report : 3471
 Page : 1 of 1 Rig or Unit :#7 **A** Inspection: Magnetic Particle
 Parts Examined: 7" ADT 65 Ton elevator S/N: 70872MA
 Surface Condition: Painted Material Temperature: 20° Celsius
 Procedure: MPI-DPJ-001 Code: ASME Section V, ASTM E709
 Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets
 Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method
 Test Medium: Magnaflex 7HF prepared bath


Test Results:

Engineer's Approval:

No defects found at time of inspection



PERMIT TO PRACTICE
FIRTH ENGINEERING LTD.
 Signature _____
 Date April 12
PERMIT NUMBER: P 6554
 The Association of Professional Engineers,
 Geologists and Geophysicists of Alberta

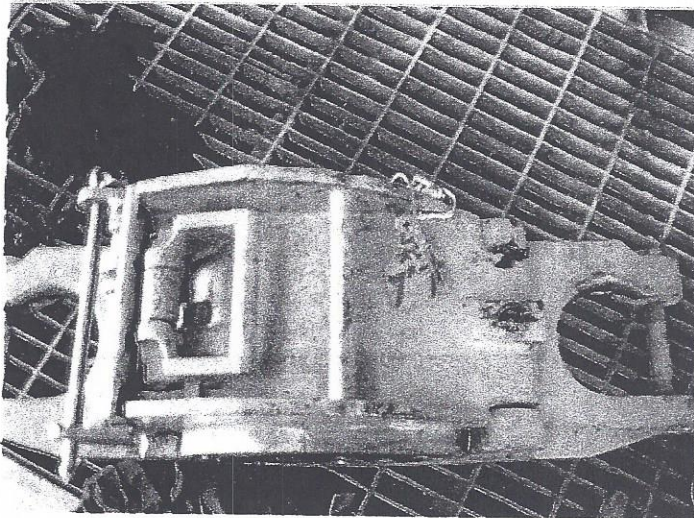

Photos:

Technician:	John Frances	CGSB #:	7062	Signature:		Assistant:	Tyler Nevison		
Repairs Complete	Yes <input type="checkbox"/>	No <input type="checkbox"/>	N/A <input checked="" type="checkbox"/>	X <input type="checkbox"/>		Acceptable For Service	Yes <input type="checkbox"/>	X <input checked="" type="checkbox"/>	No <input type="checkbox"/>
