

Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O. Box 1473
Brooks, Alberta
T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

715

INSPECTION REPORT

Client: Four Star Ventures

Location: DaPaJo Construction Limited

Date: April 05, 2012

P.O.:

Work Order: 2139d

Report: 3474

Page: 1 of 1

Rig or Unit: #15

Inspection: Magnetic Particle

Parts Examined: 7" NOI 50 Ton elevator

S/N: MAE 21529

Surface Condition: Painted

Material Temperature: 20° Celsius

Procedure: MPI-DPJ-001

Code: ASME Section V, ASTM E709

Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets



Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method

Test Medium: Magnalux 7HF prepared bath

Test Results:

No defects found at time of inspection.

Engineer's Approval:




PERMIT TO PRACTISE
FIRTH ENGINEERING LTD.

Signature:

Date:

PERMIT NUMBER: P 6554
The Association of Professional Engineers,
Geologists and Geophysicists of Alberta

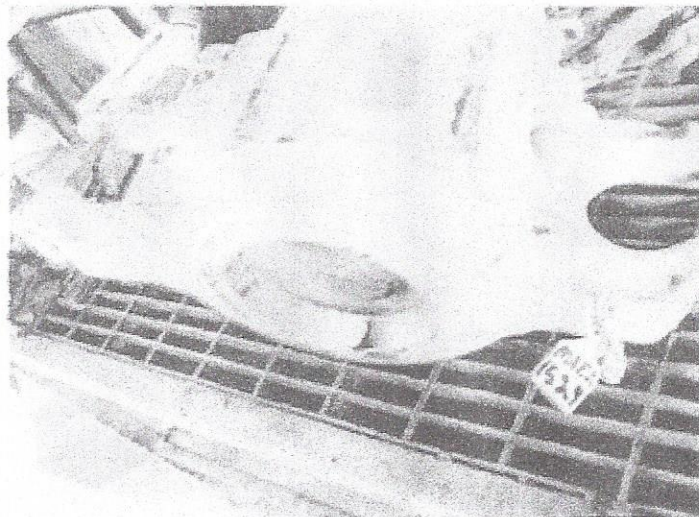

Photos:

Technician: John Frances

CGSB #: 7062

Signature:

Assistant: Tyler Nevison

Repairs Complete: Yes No

N/A

Acceptable For Service: Yes No
