

# Ideal Inspection


(a division of Ideal Oilfield Construction Ltd.)  
P.O Box 1473  
Brooks, Alberta  
T1R 1C3  
Phone: 403-362-2843 Fax: 403-362-2862

## INSPECTION REPORT

Client: Four Star Ventures	Location: DaPaJo Construction Limited	Date: April 05, 2012
P.O. :	Work Order : 2139n	Report : 3484
Page : 1 of 1	Rig or Unit :#16	Inspection: Magnetic Particle
Parts Examined: 7" elevator	S/N: 20241	
Surface Condition: Painted	Material Temperature: 20° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaflex 7HF prepared bath		

Test Results:  
No defects found at time of inspection.

Engineer's Approval:




**PERMIT TO PRACTICE**  
**FIRTH ENGINEERING LTD.**

Signature: *[Handwritten Signature]*

Date: *[Handwritten Date]*

**PERMIT NUMBER: P 6554**  
The Association of Professional Engineers,  
Geologists and Geophysicists of Alberta

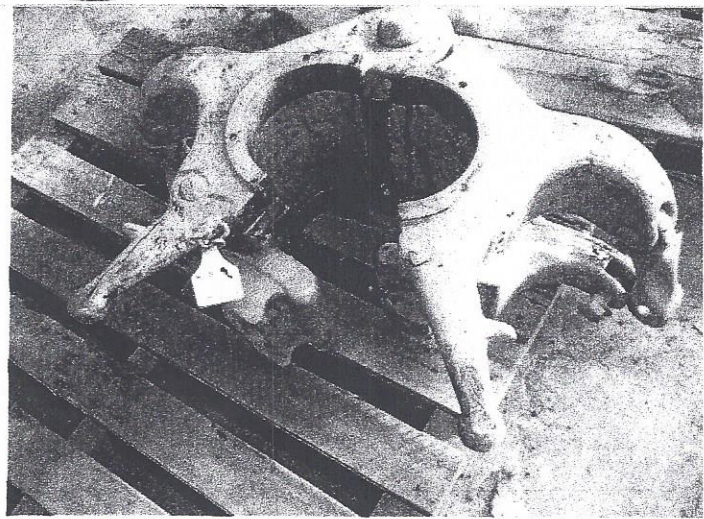

Photos:

Technician: John Frances	CGSB #: 7062	Signature: <i>[Blank]</i>	Assistant: Tyler Nevison
Repairs Complete	Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input type="checkbox"/> X <input type="checkbox"/>	Acceptable For Service	Yes <input type="checkbox"/> X <input checked="" type="checkbox"/> No <input type="checkbox"/>
