



Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)
P.O Box 1473
Brooks, Alberta
T1R 1C3
Phone: 403-362-2843 Fax: 403-362-2862

INSPECTION REPORT

Client: Four Star Ventures	Location: DaPaJo Construction Limited	Date: April 05, 2012
P.O. :	Work Order : 2139h	Report : 3478
Page : 1 of 1	Rig or Unit :#4 <i>A</i>	Inspection: Magnetic Particle
Parts Examined: 9 5/8" Web Wilson LAC 50 Ton elevator	S/N: M62792	
Surface Condition: Painted	Material Temperature: 20° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaflux 7HF prepared bath		

Test Results:

No defects found at time of inspection.

Engineer's Approval:




PERMIT TO PRACTICE
FIRTH ENGINEERING LTD.

Signature: *[Signature]*

Date: *05/04/12*

PERMIT NUMBER: P 6554
The Association of Professional Engineers,
Geologists and Geophysicists of Alberta

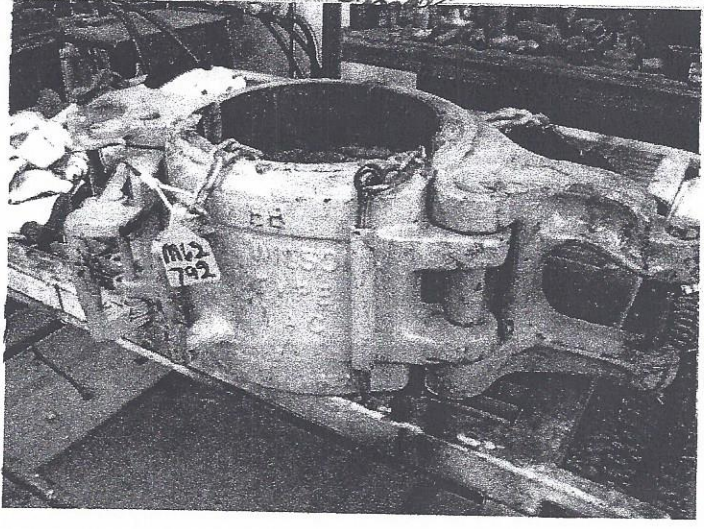

Photos:

Technician: John Frances	CGSB #: 7062	Signature: _____	Assistant: Tyler Nevison
Repairs Complete	Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input type="checkbox"/> X <input checked="" type="checkbox"/>	Acceptable For Service	Yes <input type="checkbox"/> X <input checked="" type="checkbox"/> No <input type="checkbox"/>
