

# Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)  
P.O Box 1473  
Brooks, Alberta  
T1R 1C3  
Phone: 403-362-2843 Fax: 403-362-2862





# INSPECTION REPORT

Client: Four Star Ventures	Location: DaPajo Construction Limited	Date: April 05, 2012
P.O. :	Work Order : 2139k	Report : 3481
Page : 1 of 1	Rig or Unit :#7 <b>B</b>	Inspection: Magnetic Particle
Parts Examined: 9 5/8" W+W SLX 50 Ton elevator	S/N: 50504.141	
Surface Condition: Painted	Material Temperature: 20° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaflux 7HF prepared bath		

**Test Results:**

**Engineer's Approval:**

Crack found on handle (crack repaired and elevator is ready for service)

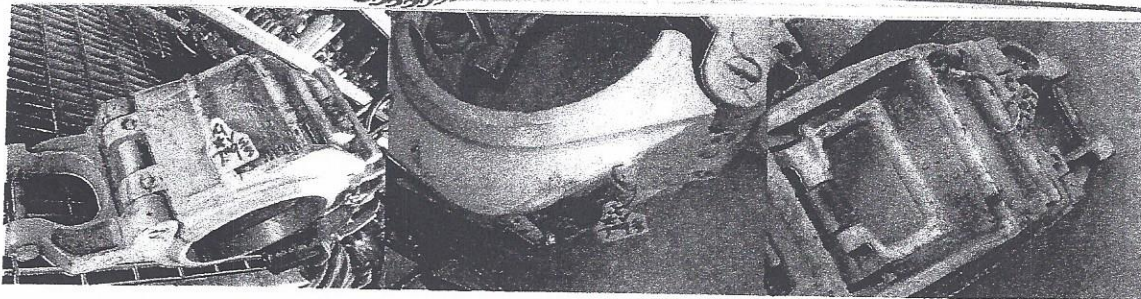

Photos:

Technician: John Frances	CGSB #: 7062	Signature:	Assistant: Tyler Nevison
Repairs Complete	Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>	N/A <input type="checkbox"/>	Acceptable For Service
			Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>
