

Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473
Brooks, Alberta
T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

INSPECTION REPORT

Client: 4 Star Ventures Ltd.	Location: DaPaJo Construction Limited	Date: Nov 27, 08
P.O.:	Work Order: 1559	Report: 2646
Page: 1 of 1	Rig or Unit: BJ YC Elevators	Inspection: Magnetic Particle
Parts Examined: BJ YC, Elevator, S/N 470		
Surface Condition: Painted	Material Temperature: 20° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B-310 Contour Probe		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaflux 14 AM Prepared Bath Florescent		

Test Results:

NO DEFECTS FOUND AT THE TIME OF THIS INSPECTION

Engineer's Approval:




PERMIT TO PRACTICE
FIRTH ENGINEERING LTD

Signature:

Date: 27 NOV 08

PERMIT NUMBER: P 6554
The Association of Professional Engineers,
Geologists and Geophysicists of Alberta

Photos

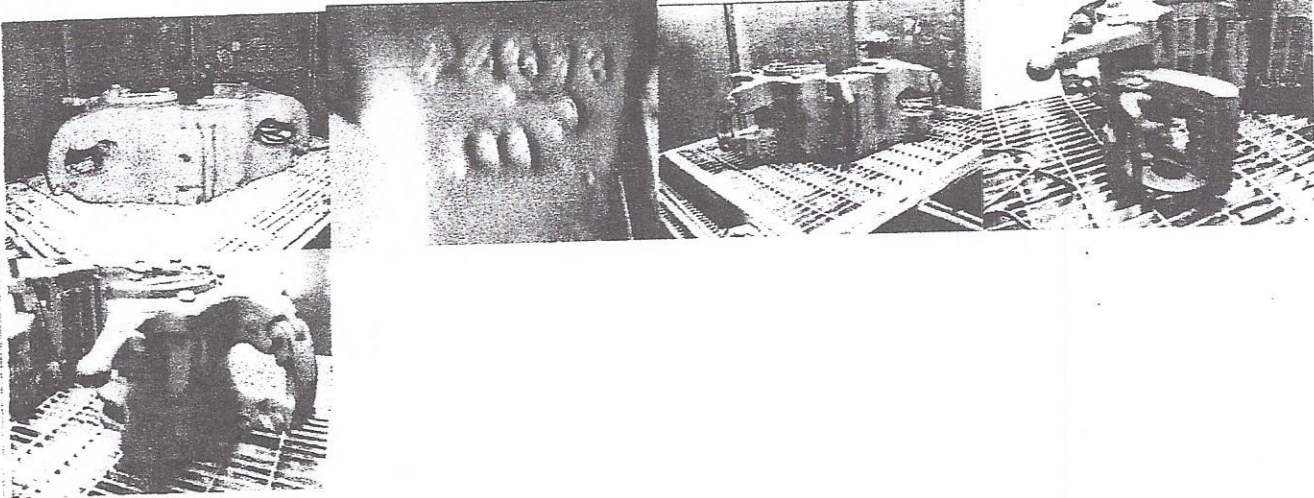

Technician: John Francis	CGSB #: 7062	Signature:	Assistant:
Repairs Complete	Yes <input type="checkbox"/> No <input checked="" type="checkbox"/>	N/A <input checked="" type="checkbox"/> X <input type="checkbox"/>	Acceptable For Service Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>
