


Ideal Inspection
 (a division of Ideal Oilfield Construction Ltd.)
 P.O Box 1473
 Brooks, Alberta
 T1R 1C3
 Phone: 403-362-2843 Fax: 403-362-2862

INSPECTION REPORT

| | | |
|--|---------------------------------------|-------------------------------|
| Client: 4 Star Ventures | Location: DaPaJo Construction Limited | Date: March 27, 2017 |
| Page: 1 of 1 | Unit : 20499 | Inspection: Magnetic Particle |
| Work Order: 2822A | Report: 4743 | |
| Parts Examined: 4 1/2 Casing Elevator | | |
| Surface Condition: Painted | Material Temperature: 8° Celsius | |
| Procedure: MPI-DPJ-001 | Code: ASME Section V, ASTM E709 | |
| Equipment: Parker B 310 Contour Probe | | |
| Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method | | |
| Test Medium: Magnaglo 14AM prepared bath | | |


Test Results:
NO DEFECTS WERE FOUND AT THE TIME OF THIS INSPECTION

Engineer's Approval:



[Signature]
 May 23, 2017

Photos:

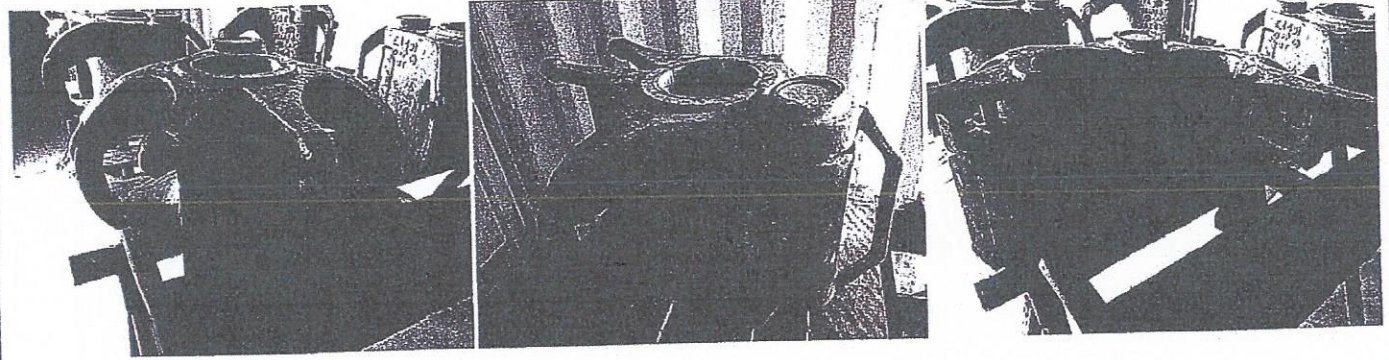

| | | | |
|---------------------------|--|--|--------------------------|
| Technician: Bryan Hoskins | CGSB #: 19053 | Signature: <i>[Signature]</i> | Assistant: Travis Bungay |
| Repairs Complete | Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input checked="" type="checkbox"/> | Acceptable For Service Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> | |
