

# Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473

Brooks, Alberta

T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

703

## INSPECTION REPORT

Client: 4 Star Ventures	Location: DaPaJo Construction Limited	Date: March 27, 2017
Page: 1 of 1	Unit : CT30	Inspection: Magnetic Particle
Work Order: 2822E	Report: 4747	
Parts Examined: 7" BJ Casing Elevator		
Surface Condition: Painted	Material Temperature: 8° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaglo 14AM prepared bath		

Test Results:
<b>NO DEFECTS WERE FOUND AT THE TIME OF THIS INSPECTION</b>


Engineer's Approval:



*[Signature]*

May 23, 2017

Photos:

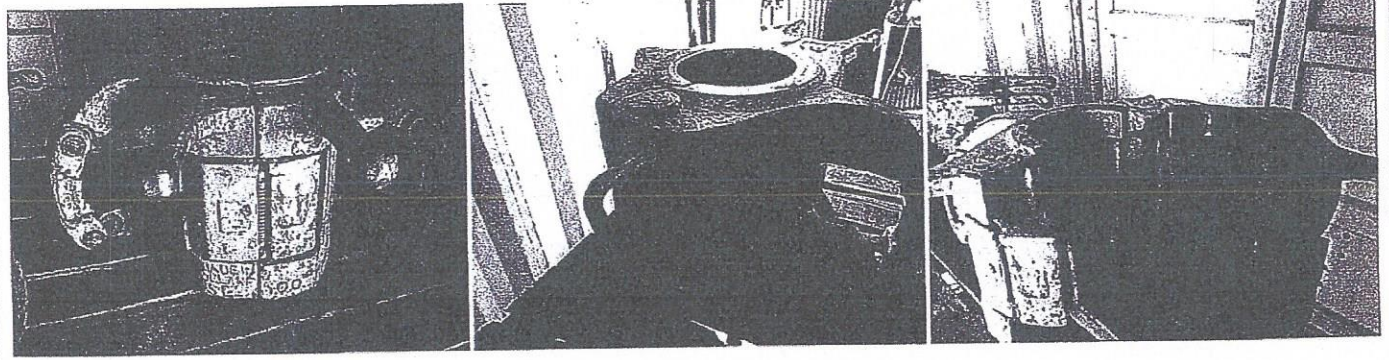

Technician:	Bryan Hoskins	CGSB #:	19053	Signature:	<i>[Signature]</i>	Assistant:	Travis Bungay		
Repairs Complete	Yes <input type="checkbox"/>	No <input type="checkbox"/>	N/A <input type="checkbox"/>	X <input checked="" type="checkbox"/>	Acceptable For Service		Yes <input type="checkbox"/>	X <input checked="" type="checkbox"/>	No <input type="checkbox"/>
