

Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473

Brooks, Alberta



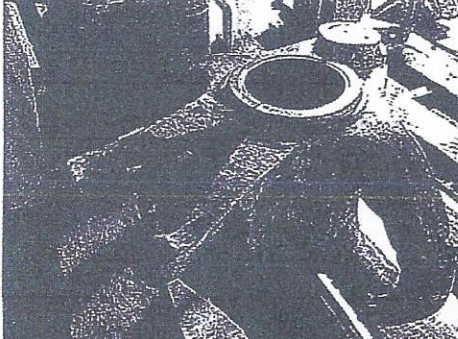



T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

406

INSPECTION REPORT

Client: 4 Star Ventures		Location: DaPaJo Construction Limited		Date: March 27, 2017	
Page: 1 of 1		Unit : 78974		Inspection: Magnetic Particle	
Work Order: 2822B		Report: 4744			
Parts Examined: 4 1/2 AOT Casing Elevator					
Surface Condition: Painted			Material Temperature: 8° Celsius		
Procedure: MPI-DPJ-001			Code: ASME Section V, ASTM E709		
Equipment: Parker B 310 Contour Probe					
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method					
Test Medium: Magnaglo 14AM prepared bath					
Test Results:			Engineer's Approval:		
NO DEFECTS WERE FOUND AT THE TIME OF THIS INSPECTION			  May 23, 2017		
Photos:					
					
Technician: Bryan Hoskins		CGSB #: 19053		Signature: 	
Assistant: Travis Bungay					
Repairs Complete	Yes <input type="checkbox"/>	No <input type="checkbox"/>	N/A <input type="checkbox"/>	X <input checked="" type="checkbox"/>	Acceptable For Service
Yes <input type="checkbox"/>		X <input checked="" type="checkbox"/>		No <input type="checkbox"/>	
